S - CURVE

A) Improvement to Shahapur Shenwa Dolkhamb Chondha Sangamner Shegaon Nanded Dharmabad Road SH-50 Km.0.00 to 38.00 in Tal. Shahapur, Dist. Thane on hybrid Annuity Basis.
(B) Improvement to kambare Piwali NH-3 to Washind Road MDR-57 Km.0.00 to 23.600 in Tal. Shahapur, Dist. Thane on hybrid Annuity Basis.
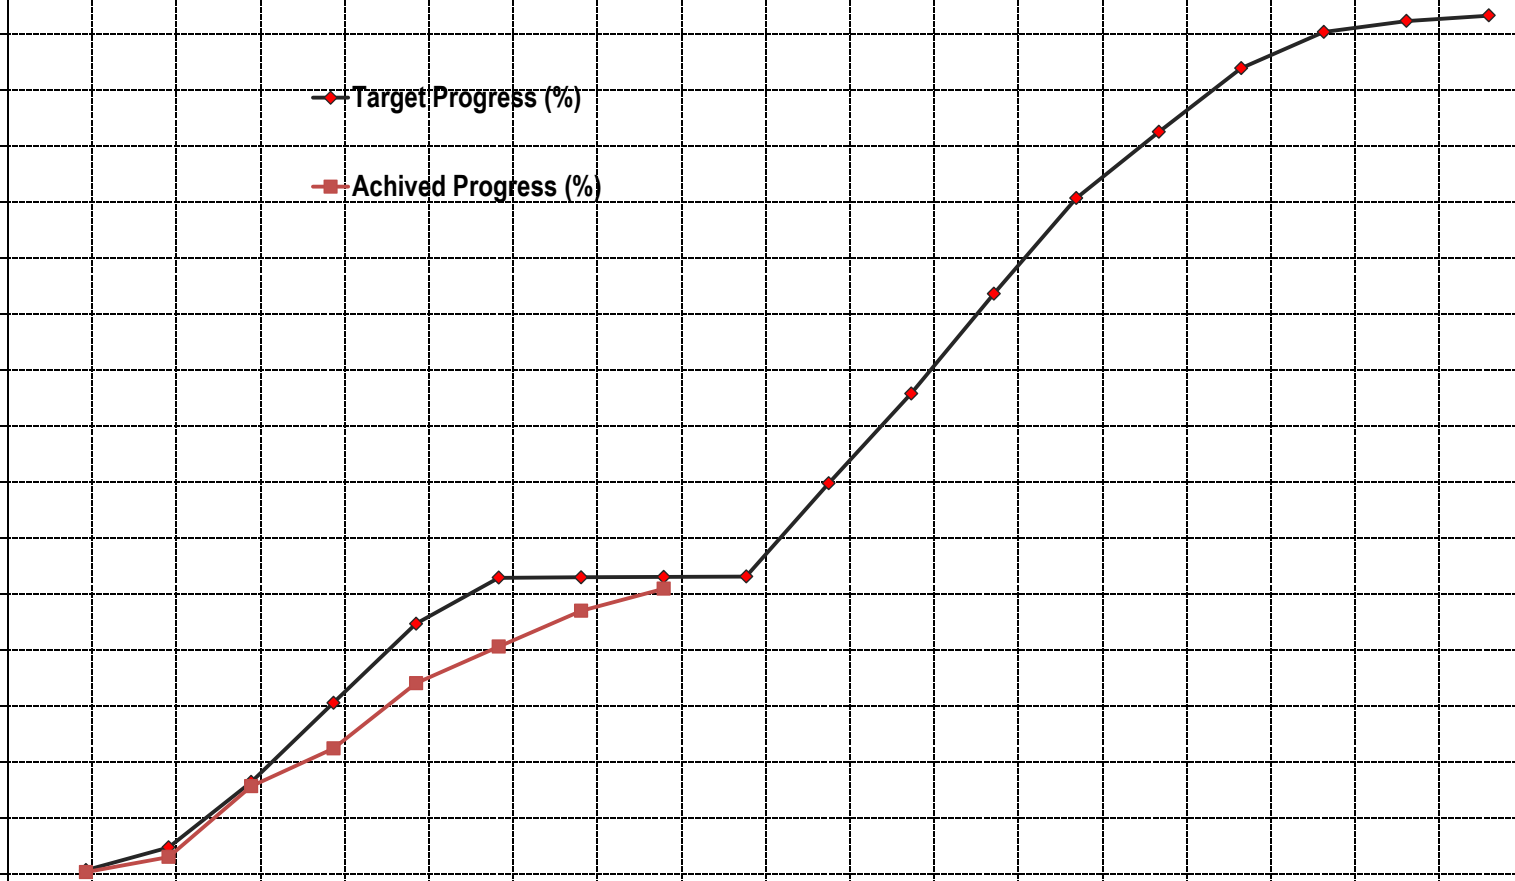
Sl. No	Activity	Jan-19	Feb-19	Mar-19	Apr-19	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19	Nov-19	Dec-19	Jan-20	Feb-20	Mar-20	Apr-20	May-20	Jun-20
1	Earthwork																		
2	GSB																		
3	WMM																		
4	DBM																		
5	BC																		
6	BM																		
7	Hard shoulder																		
8	Pipe Culvert																		
9	Slab Culvert																		
10	Minor Bridge																		
11	Major Bridge																		
12	Traffic Sigs & Other Appurtenances																		
13	Km. STONES, BOUNDARY STONE, ETC.																		
14	Concrete work																		
15	Bus Bay																		
16	Miscellaneous (Site clearance, Quality Control,Crust removal/																		
17	Road side plantation																		
18	Toe wall /retaining wall																		
Target Progress (%)	Monthly	0.57%	2.65%	7.61%	9.21%	9.21%	5.36%	0.04%	0.04%	0.04%	10.86%	10.44%	11.60%	11.15%	7.70%	7.41%	4.21%	1.27%	0.64%
	Cummul.	0.57%	3.22%	10.82%	20.03%	29.23%	34.59%	34.63%	34.68%	34.72%	45.58%	56.02%	67.62%	78.77%	86.47%	93.88%	98.09%	99.36%	100.00%
Achived Progress (%)	Monthly	0.35%	1.75%	8.24%	4.38%	7.60%	4.26%	4.16%	2.57%										
	Cummul.	0.35%	2.10%	10.34%	14.72%	22.32%	26.58%	30.74%	33.31%
